


ID	Task Name	Duration	Start	Finish	Predecessors	'21 Nov 22	'21 Nov 29	'21 Dec 06	'21 Dec 13	'21 Dec 20	'21 Dec 27	'22 Jan 0
1	On hard	3 days	Nov 22	Nov 24		S	M	T	W	T	F	S
2	Touch up antifoul	1 day	Nov 22	Nov 22								
3	Inspect sealing for depth sounder	0,5 days	Nov 23	Nov 23	2							
4	Leave sewingmashine for service	3 days	Nov 22	Nov 24								
5	In marina	14 days	Nov 25	Dec 08	1							
6	Fix cradle for liferaft	1 day	Nov 25	Nov 25								
7	Attachment for lifering	1 day	Nov 25	Nov 25								
8	Davits swingpreventers	1 day	Nov 25	Nov 25								
9	Reinforce cleatplates	1 day	Nov 25	Nov 25								
10	Put up sails	1 day	Nov 25	Nov 25								
11	Clean deck	1 day	Nov 26	Nov 26	10							
12	Clean and unpack inside	1 day	Nov 27	Nov 27	11							
13	Fix bimini	3 days	Nov 28	Nov 30	12							
14	Fix Sprayhood	3 days	Dec 01	Dec 03	13							
15	Make side canvas	3 days	Dec 04	Dec 06	14							
16	Fix leaks in dinghy	2 days	Dec 07	Dec 08	15							
17	Build diesel polisher	2 days	Nov 28	Nov 29	12							
18	Inspect/change mixing elbow	1 day	Nov 30	Nov 30	17							
19	Change impeller nuts to brass	1 day	Dec 01	Dec 01	18							
20	Clean and lube steering chain and pulleys	1 day	Dec 02	Dec 02	19							
21	Inspect and shorten forestay	2 days	Dec 03	Dec 04	20							
22	Service genoa furler	1 day	Dec 05	Dec 05	21							
23	At anchor	17,5 days	Dec 09	Dec 26	5							
24	Fix small windows	1 day	Dec 09	Dec 09								
25	Set up preventer line	1 day	Dec 10	Dec 10	24							
26	Water recovery system	3 days	Dec 11	Dec 13	25							
27	Fans in bedroom and salon	2 days	Dec 14	Dec 15	26							
28	Bilge alarm	2 days	Dec 16	Dec 17	27							
29	Install new inverter	2 days	Dec 18	Dec 19	28							
30	Protection for water in anchorboc	1 day	Dec 20	Dec 20	29							
31	Fix rust on waterheater bolts	2 days	Dec 21	Dec 22	30							
32	Fix bowthruster switch	0,5 days	Dec 23	Dec 23	31							
33	Put up smoke detectors	0,5 days	Dec 23	Dec 23	32							
34	Install electric valve for gas	1 day	Dec 24	Dec 24	33							
35	Service winches	1 day	Dec 25	Dec 25	34							
36	Vaseline valves	0,5 days	Dec 26	Dec 26	35							



Project: Prep s2
Date: Jul 26

Task

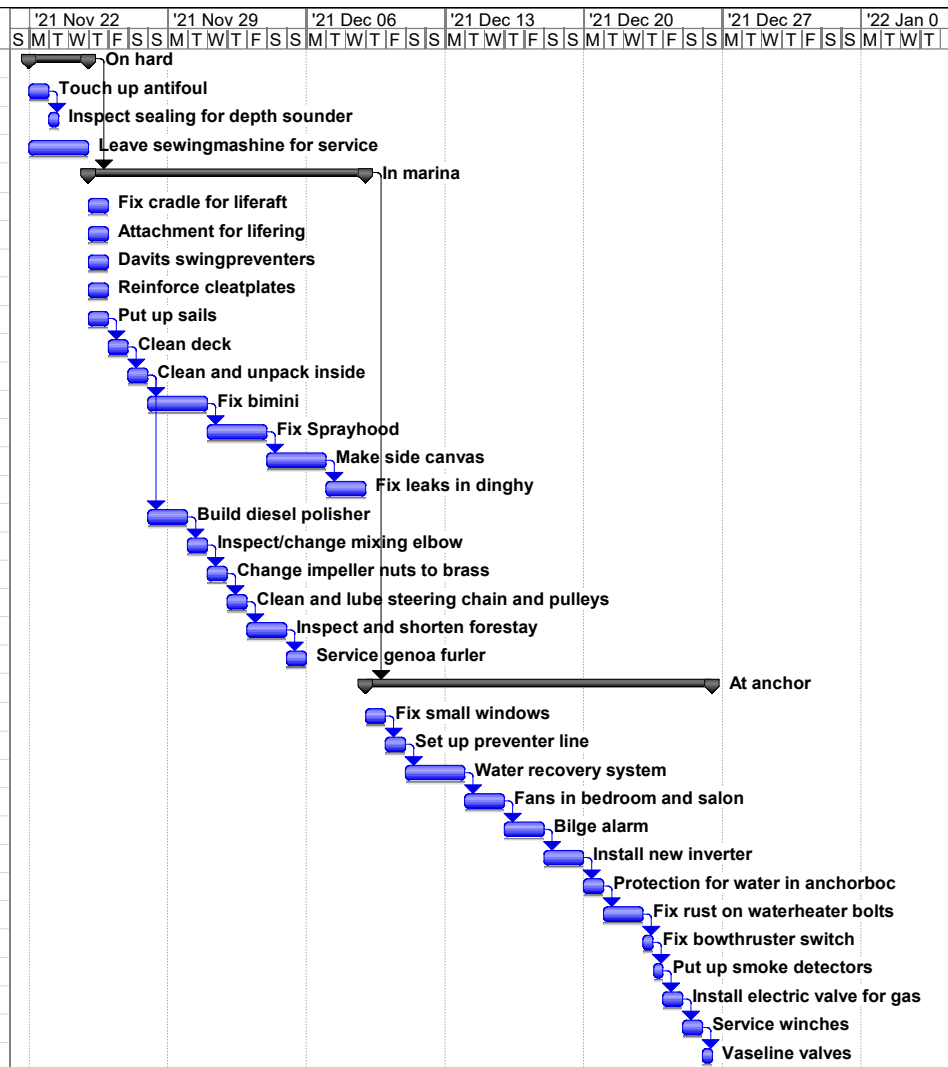

Milestone



External Tasks



Split



Summary



External Milestone



Progress



Project Summary



Deadline

